

Instructions

Please download this Word document (available on the Industrial Commission/Outdoor Heritage Fund Program website at <http://www.nd.gov/ndic/outdoor-infopage.htm>) to your computer and provide the information as requested. You are not limited to the spacing provided. After completing the report, save it and attach it to an e-mail and send it to outdoorheritage@nd.gov AND print it and mail it to: North Dakota Industrial Commission, ATTN: Outdoor Heritage Fund Program, State Capitol – Fourteenth Floor, 600 East Boulevard Ave. Dept. 405, Bismarck, ND 58505. If you are unable to scan attachments, mail them with your paper copy of the report. You will be sent a confirmation by e-mail of receipt of your report and attachments.

**Outdoor Heritage Fund
Status and Final Report Form/Guidelines**

This report is used to show progress of grant projects funded through the Outdoor Heritage Fund. Status Reports and the Final Report must be submitted as required in Contract.

Contract Number	Report Date	Period Covered by Report
022-019	8/16/17	(1/30/17 to 8/1/17)

Project Name
Bald Hill Creek Watershed Project

Project Sponsor Name
Griggs County Soil Conservation District

Responsible Official (Last, First Middle)	Responsible Official's Title
Johnson, Nathan John	District Manager

Project Sponsor Address
PO Box 526

City	State	Zip Code	Telephone Number
Cooperstown	ND	58425	701-797-2240

Financial Update
Please provide the following information regarding the funding for your project based on the contract award:

Funds Spent this Reporting Period
(As appropriate please provide copies of receipts for purchases)
Match Funding \$ 1840.16
In-kind Funding \$ 0
OHF Funding **Requested for Reimbursement \$2760.24**
Total Funding Expended for this Reporting Period \$4600.40

Total Funds Spent to Date
Match Funding \$46,450.58
In-kind Funding \$0
OHF Funding Received and Requested for Reimbursement \$69,675.87
Total Funding Expended to Date \$116,126.44

Balance of Grant Funds
Match Funding \$153,549.42
In-kind Funding \$0
OHF Funding still to be Requested \$228,208.38
Total Funding to be Expended on this Project \$500,000

Do you anticipate needing to request a grant extension If yes, please explain
/_/ Yes /x/ No

Work Completed during Period Covered by Report:


(This information will be posted on the Outdoor Heritage Fund/Industrial Commission website)

Producers have completed 2 contracts that I have paid out on. Ron Eggermont has completed 40.7 acres of hay planting that he will use to help feed his cattle. He received a cost share of \$1269.84 with the total project cost of \$2116.40. Jeff Edland completed a fencing project that included 1380 ft. of fence. He received cost share of \$1490.40 with the total project cost of \$2484.00. This project allows Jeff to keep his cattle out of a waterway that flows to Bald Hill Creek.

I have several contracts that are signed that are waiting to be completed that include Partial Manure Management System, fence, pipeline, water tanks, and well. These projects will receive a cost share of \$84,320.91 with the total projects cost of \$140,534.85. They will be paid as practices are completed.

Photos of work completed are welcome (If appropriate, please submit photos of key elements of the project completed or in progress during reporting period) Do not exceed five photos per project report.

Signature of Responsible Official



8/16/17

The project reports shall be provided to the Commission in both electronic and hard-copy formats with permission for unrestricted distribution. The electronic versions shall be in a suitable format for posting on the Outdoor Heritage Fund/Commission website.


FENCE DATA

Name: Jeff Edland Plan/Contract No. 319-2-17 Field #'s _____

Type of Fence: **General Purpose (4 wire barbed)**

	Planned	Applied
Length of Fence	2150	1380
Wire		
Type:	two tipped barbed	two tipped barbed
Number of wires	4	4
Height and/or spacing	See Job Sheet 13	See Job Sheet 13
Gauge and galvanization	12.5 gauge wire 14 gauge barbs	12.5 gauge wire 14 gauge barbs
Tensile strength	Standard weight	Standard weight
Mesh size	NA	NA
Wire fasteners (type)	Staples 9 gauge wire staples 1.5 in.	9 gauge wire staples 1.5 in.
	Ties/clips #12 galvanized wire or post type	#12 galvanized wire or post type
	Insulators NA	NA
Line Posts		
Type	Wood 3 in. dia., 6 ft. long, and straight	3 in. dia., 6 ft. long, and straight
	Steel New 5.5 ft. w/anchor plate (1.25 lbs./ft.)	New 5.5 ft. w/anchor plate (1.25 lbs./ft.)
	Fiberglass NA	NA
Depth	Sand 24 in.	24 in.
	Other soil textures 18 in.	18 in.
Spacing	Up to 24 ft.	up to 24 in.
Corner, Gate, Brace Assembly		
Type	H-brace	H-brace
Posts	Wood rot resistant - 7 ft. X 5 in. dia., straight	rot resistant - 7 ft. X 5 in. dia., straight
Depth	30 in.	30 in.
Line brace spacing	less than 1320 ft.	less than 1320 ft.
Line and gate brace assembly	See Job Sheet 13	see pic
Corner and gate brace assembly	See Job Sheet 13	see pic
Brace material	Wood rot resistant 8 ft. 4X4 or 4 in. dia. round	rot resistant 8 ft. 4X4 or 4 in. dia. round
	Steel galvanized 2 in. x 8 ft. steel pipe	NA
Energizer		
Peak voltage output	N/A	NA
Pulse duration	N/A	NA
Pulses per minute	N/A	NA
Grounding	N/A	NA
Lightning arrestor	N/A	NA
Safety-pace fuse	N/A	NA
Overhead or underground wire	N/A	NA

Location Map

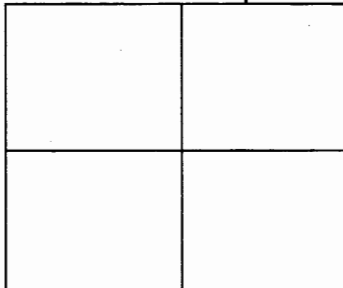

Sec. 31

Twp. 147

Rng. 62

Planning Assistance By:

Nathan Johnson
 Name and Date

Practice meets
 Standards and
 Specifications

Yes No

Certified By:
Nathan Johnson
 Name and Date

Arrowwood Prairie Co-op Sutton
120 99th Ave SE
Sutton ND 58484
701-769-2334 Fax: 701-769-2340

Invoice

2001211

Invoice Date 06/06/2017
Due Date 06/09/2017

Customer ID 199291

Shipping Loc. 02

Ticket(s) 5723

Ron Eggermont
10041 4th St NE
Binford, ND 58416

Comments: ka

Quantity	Description	Unit Price	Total \$
10.000 Bags	Alfalfa Legendary Lot# N284-16CVS	262.00 /Bags	2,620.00 Book
200.000 Lbs	Brome Grass Lot# 1181	3.55 /Lbs	710.00 Book

Sub Total 3,330.00

Amount Due 3,330.00
