

## Instructions

Please download this Word document (available on the Industrial Commission/Outdoor Heritage Fund Program website at <http://www.nd.gov/ndic/outdoor-infopage.htm> ) to your computer and provide the information as requested. You are not limited to the spacing provided. After completing the report, save it and attach it to an e-mail and send it to [outdoorheritage@nd.gov](mailto:outdoorheritage@nd.gov) AND print it and mail it to: North Dakota Industrial Commission, ATTN: Outdoor Heritage Fund Program, State Capitol – Fourteenth Floor, 600 East Boulevard Ave. Dept. 405, Bismarck, ND 58505. If you are unable to scan attachments, mail them with your paper copy of the report. You will be sent a confirmation by e-mail of receipt of your report and attachments.

| Outdoor Heritage Fund<br>Status and Final Report Form/Guidelines  |                    |  |   |
|---|--------------------|--|---|
| This report is used to show progress of grant projects funded through the Outdoor Heritage Fund. Status Reports and the Final Report must be submitted as required in Contract. |                    |  |   |
| Contract Number   | Report Date        | Period Covered by Report<br>(xx/xx/xx to xx/xx/xx) |   |
| 011-125   | 10/24/2018         | 05/01/2018-10/24/2018                              |   |
| Project Name<br><b>Public Accessible Sensory Garden</b>   |                    |  |   |
| Project Sponsor Name<br><b>Jamestown Parks &amp; Recreation Foundation</b>  |                    |  |   |
| Responsible Official (Last, First Middle)<br><b>Hogan, Doug</b>   |                    | Responsible Official's Title<br><b>Director</b>    |   |
| Project Sponsor Address<br><b>1002 2<sup>nd</sup> Ave SE</b>  |                    |  |   |
| City<br><b>Jamestown</b>  | State<br><b>ND</b> | Zip Code<br><b>58401</b>                           | Telephone Number<br><b>701-252-3982</b> |
| <b><u>Financial Update</u></b>  |                    |  |   |
| Please provide the following information regarding the funding for your project based on the contract award:  |                    |  |   |
| <b><u>Funds Spent this Reporting Period</u></b>   |                    |  |   |
| (As appropriate please provide copies of receipts for purchases)  |                    |  |   |
| Match Funding \$ 2,850.00 <b>\$605.95</b>   |                    |  |   |
| In-kind Funding \$ 9,394.50 <b>\$13,057.00</b>  |                    |  |   |
| OHF Funding <b>Requested for Reimbursement</b> \$18,000.00 <b>\$15,502.08</b>   |                    |  |   |
| Total Funding Expended for this Reporting Period \$30,244.50 <b>\$29,165.03</b>   |                    |  |   |
| <b><u>Total Funds Spent to Date</u></b>   |                    |  |   |
| Match Funding \$ 2,850.00 <b>*Same as above</b>   |                    |  |   |
| In-kind Funding \$ 9,394.50   |                    |  |   |
| OHF Funding Received and Requested for Reimbursement \$ 18,000.00   |                    |  |   |
| Total Funding Expended to Date \$ 30,244.50   |                    |  |   |
| <b><u>Balance of Grant Funds</u></b>  |                    |  |   |
| Match Funding \$ 0.00 <b>\$12,455.05</b>  |                    |  |   |
| In-kind Funding \$ 0.00 <b>\$1,153</b>  |                    |  |   |
| OHF Funding still to be Requested \$ 15,000.00 <b>\$17,497.92</b>   |                    |  |   |
| Total Funding to be Expended on this Project \$ 33,000.00 <b>\$13,608.05</b>  |                    |  |   |
| Do you anticipate needing to request a grant extension    If yes, please explain<br>/ _ / Yes    / x / No   |                    |  |   |

**Work Completed during Period Covered by Report:**

(This information will be posted on the Outdoor Heritage Fund/Industrial Commission website)

Handy Dan was contracted to complete the wheelchair pads and was completed in June 2018. Total cost \$4778.00

May, June, July, August, September 2018 all plants were ordered (909 plants) and planted by over 10 volunteers. Supplies were bought including new pump for water tank, metal landscape edging, Miracle grow, Round Up, potting soil, etc.  
Watering was done by volunteers the entire summer.

Naming rights for all planters and benches were offered to the community, 28 planters and 5 benches. All were sold but 4 planters. Name plaques were engineered at Agri Cover Manufacturing, engraving company emblem or logos with each company name on each plaque. All material, engineering and engraving donated. Each plaque cost \$100 times 29 plaques= \$2900 in kind donation.

Electrical contractor was contracted to install electrical line, which was completed in July 2018. Cost \$1644.00


Builders FirstSource provided material and Opp'n Hammer Handyman completed the boardwalk in August 2018. Total cost \$5092.40

Kiosk was contracted by Roughriders Sign and Designs and installed in September 2018 with maps and donors to be added in the Spring 2019. Cost \$3811.60, in-kind donation.  
Two large picnic table and one small table in kind donation from Modern Woodman.

In the process of getting bids to complete a water feature that will be installed in the Spring of 2019.

Photos of work completed are welcome (If appropriate, please submit photos of key elements of the project completed or in progress during reporting period) Do not exceed five photos per project report.

Signature of Responsible Official



The project reports shall be provided to the Commission in both electronic and hard-copy formats with permission for unrestricted distribution. The electronic versions shall be in a suitable format for posting on the Outdoor Heritage Fund/Commission website.























# Serving others

## Helping others lifelong career for Jamestown woman

By Keith Norman  
The Jamestown Sun

Seeing the sense of accomplishment in the eyes of her clients helps Beth Dewald, independent living advocate for Freedom Resource Center, find joy in her job.

"Being able to help an individual with their needs or recover from a catastrophic event or help people advocate for themselves is wonderful," she said. "Helping empower people is the best reward that you see in their accomplishments."

Dewald is in her fourth year with Freedom Resource Center.

"The organization is phenomenal," she said. "We work on advocacy and helping people grow within themselves."

Freedom Resource Center helps people with disabilities with the intent of solving problems that can help them live as independently as possible. That process also involves working with businesses and government organizations that employ or provide services to those with disabilities.

Dewald said Freedom Resource Center's involvement in the Jamestown Sensory Garden started with concerns for accessibility.

"The Freedom Resource Center does activities every

“

*I'm glad I left and glad I came back. It gave me the confidence to bring ideas to the table and implement them.*

— BETH DEWALD

month," she said. "We wanted to go the (city) parks but we couldn't because of a lack of (bathroom) access."

The Sensory Garden, located in Solien-Denault Park, incorporates a number of features to make the park experience more enjoyable for people of all abilities. The planters are at varying heights allowing people walking or using a wheelchair to enjoy an up-close experience with the plants. The plants themselves were selected to provide visual, texture and scent experiences.

"We will share more information with parks on bathroom and playground accessibility in the future," Dewald said.




John M. Steiner / The Sun

Beth Dewald, independent living advocate for Freedom Resource Center, sits in the Jamestown Sensory Garden that her organization helped plan. In the background are planters at varying heights to provide opportunities for people of all abilities to enjoy the senses of sight, smell and touch.

DEWALD: Page 6

## THANK YOU

Thank you to the women of North Dakota Farmers Union and Farmers Union Insurance for your hard work and commitment. Your dedication and service to members and insureds is one of the driving forces behind our success.

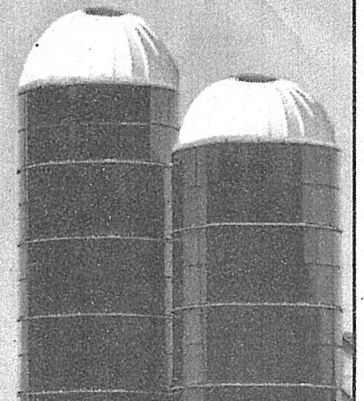





Jamestown Area Chamber  
of Commerce  
City Beautification Committee

In Loving Memory of  
Harold Newman,  
a lover of trees.  
by Kari Newman Ness

Mix 6600  
KSJB



9/27/18

