

Instructions

Please download this Word document (available on the Industrial Commission/Outdoor Heritage Fund Program website at <http://www.nd.gov/ndic/outdoor-infopage.htm>) to your computer and provide the information as requested. You are not limited to the spacing provided. After completing the report, save it and attach it to an e-mail and send it to outdoorheritage@nd.gov AND print it and mail it to: North Dakota Industrial Commission, ATTN: Outdoor Heritage Fund Program, State Capitol – Fourteenth Floor, 600 East Boulevard Ave. Dept. 405, Bismarck, ND 58505. If you are unable to scan attachments, mail them with your paper copy of the report. You will be sent a confirmation by e-mail of receipt of your report and attachments.

Outdoor Heritage Fund Status and Final Report Form/Guidelines			
This report is used to show progress of grant projects funded through the Outdoor Heritage Fund. Status Reports and the Final Report must be submitted as required in Contract.			
Contract Number	Report Date	Period Covered by Report (xx/xx/xx to xx/xx/xx)	
010-113	6/12/2018	4/1/2018 to 6/11/2018	
Project Name Tree & Wildlife Cover Restoration			
Project Sponsor Name Velva Wildlife Club			
Responsible Official (Last, First Middle)		Responsible Official's Title	
D.J. Randolph		Velva Wildlife Club Treasurer	
Project Sponsor Address 4320 Trappers Lane #17			
City	State	Zip Code	Telephone Number
Velva	ND	58790	701-720-2134
<u>Financial Update</u>			
Please provide the following information regarding the funding for your project based on the contract award:			
<u>Funds Spent this Reporting Period</u>			
(As appropriate please provide copies of receipts for purchases)			
Match Funding \$ 3,186 for trees, stakes & tubes. 0			
In-kind Funding \$ 952.50 in kind services for site prep and tree staking. @ 1,005.00			
OHF Funding Requested for Reimbursement \$ 3,186 \$ 2,867.40			
Total Funding Expended for this Reporting Period \$ 4,138.50			
<u>Total Funds Spent to Date</u>			
Match Funding \$ 3,186 for trees, stakes & tubes.			
In-kind Funding \$ 952.50 in kind services for site prep and tree staking.			
OHF Funding Received and Requested for Reimbursement \$ 3,186			
Total Funding Expended to Date \$ 4,138.50			
<u>Balance of Grant Funds</u>			
Match Funding \$ 0			
In-kind Funding \$ 750 over 3 years for weed badgering service.			
OHF Funding still to be Requested \$ 0 \$ 318.40			
Total Funding to be Expended on this Project \$ 4,888.50			
Do you anticipate needing to request a grant extension If yes, please explain			
<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No			

Exhibit B

Work Completed during Period Covered by Report:

(This information will be posted on the Outdoor Heritage Fund/Industrial Commission website)

Site prep in early May included plowing planting area with small tractor and 2 bottom plow. Site was then tilled with small tractor 3 times to get soil in best condition to plant.

South McHenry Soil Conservation District planted trees on 5/21/2018.

Trees were watered on 5.22/2018 and on 5/29/2018. Trees were staked on 6/3/2018. We will wait till fall to install tubes to prevent over heating during summer months.

Weed badgering will be performed late summer/early fall 2018, 2019 and 2020.

Photos of work completed are welcome (If appropriate, please submit photos of key elements of the project completed or in progress during reporting period) Do not exceed five photos per project report.

Signature of Responsible Official

The project reports shall be provided to the Commission in both electronic and hard-copy formats with permission for unrestricted distribution. The electronic versions shall be in a suitable format for posting on the Outdoor Heritage Fund/Commission website.

ND - NRCS

EASTERN ND - TREE AND SHRUB PLANTING WORKSHEET

Name: **Valva Wildlife Club**


Address:

Valva, ND 58790

Phone #: 720-2134

ND-CPA-4, Rev. 02-2017

Plan Sketch Map

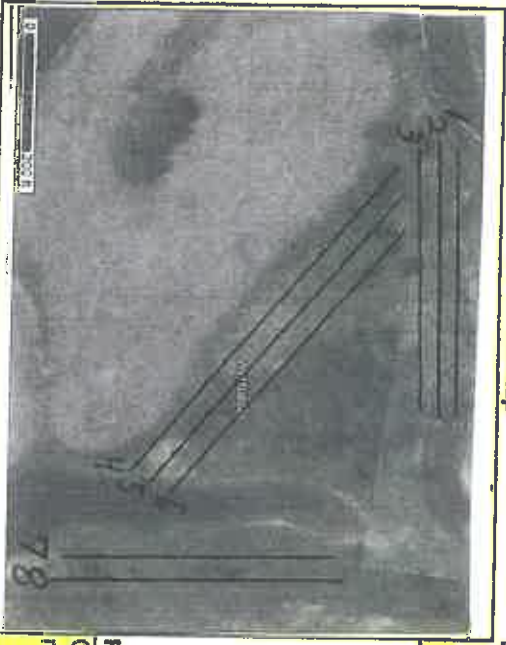

Quarter/Half: **NW 1/4**

Section: **17**

Township: **153**

Planned by: **Yelvo**

Range: **80**

Date: **10/5/2017**

Planned Soil Mapunit / name component(s): **F575A**

Approved by:

Date:

Conservation Tree & Shrub Group: **5**

Planned by:

Select MLRA: **55A**

Landuse: **Wildlife**

Approved by:

Program: **None**

Type of Planting: **New**

Approved by:

Protected from livestock? **Yes**

Site Preparation: **Tilled/Herbicide**

Approved by:

Site conditions at planting time:

Spacing between rows: **16** feet

Distance from Windward row to roads or bldgs. **NA** feet

(Minimum 200' on N & W, and 100' on S & E)

Remarks on site prep, conditions and management (Weed Control) Date:

Cottonwood, Eastern - grows on a variety of soil types but prefers well-drained sands or silts along river bottoms. There are well established cottonwoods growing near by.

Check Out By: _____ Date: _____

This practice installation **MEETS / DOES NOT MEET** the ND FOTG standards and specifications. (circle one)

Certified By: _____ Date: _____

Planting No.	Planned Length	Planned Length	Planned Width	Acres	Row #	Primary Species of Tree or Shrub	Type or Variety	Alternating Species	Planned Spacing in row	Row Spacing (installed)	Number Planned (est)	Number Planted (installed)	Primary Specie / CTSG	Alternating Specie / CTSG		
1	440		18	0.2	1	Ash, Green			12		37		suitable			
1	440		16	0.2	2	Oak, Bur			12		37		suitable			
1	440		18	0.2	3	Cherry, Nanking			9		55		suitable			
2	500		18	0.2	4	Cottonwood, Eastern			12		42		NR			
2	500		16	0.2	5	Ash, Green			12		42		suitable			
3	500		18	0.2	6	Plum, American			9		63		suitable			
3	400		18	0.2	7	Ash, Green			12		34		suitable			
3	400		18	0.2	8	Crabapple, Siberian			10		40		suitable			
Totals											3620	140	1.5	350		



Contact us [Subscribe](#) [Archived Soil Surveys](#) [Soil Survey Status](#) [Glossary](#) [Preferences](#) [Link](#) [Logout](#) [Help](#)

Area of Interest (AOI) [Soil Map](#) [Soil Data Explorer](#) [Download Soils Data](#) [Shopping Cart \(Free\)](#)

A A A



[Printable Version](#) [Add to Shopping Cart](#)

Search

Map Unit Legend

McHenry County, North Dakota (ND049)
McHenry County, North Dakota (ND049)

Map Unit Symbol	Map Unit Name	Acres in AOI	Percent of AOI
F527A	Ludden silty clay, very poorly drained, 0 to 1 percent slopes, frequently flooded	0.9	14.1%
F576A	Velva loam, moist, 0 to 2 percent slopes, occasionally flooded	5.2	85.9%
Totals for Area of Interest		6.1	100.0%

Soil Type	Soil Name	Soil %	Suitability Group
F576A	Velva	89	5
	La Prairie	9	1
	Ludden	2	2k

Soil Map



Warning: Soil Map may not be valid at this scale.
You have zoomed in beyond the scale at which the soil map for this area is intended to be used. Mapping of soils is done at a particular scale. The soil surveys that comprise your AOI were mapped at 1:20,000. The design of map units and the level of detail shown in the resulting soil map are dependent on that map scale. Enhancement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show small areas of contrasting soils that could have been shown at a more detailed scale.

